A daily system for inquiries and appointments

Program owner: Wyline | Immediate priority: first qualified inquiry, first booked appointment, first held conversation.

40	20	15	6	750
Qualified inquiries	**Booked appointments**	**Held conversations**	**Trial cases received**	**Verified contacts**
Proposed working target	Reset outcome target	20 x 75% attendance	Reset outcome target	Qualified outreach input

HOW THE DAY WORKS

01 / Commit

Each owner sees the dated deliverable, target, dependency and definition of done.

02 / Execute

Work the highest-priority conversion task. Record output and link the evidence.

03 / Review

Wyline accepts the result or returns it with a specific correction and owner.

04 / Recover

Blocked or missed work stays visible with help, a recovery owner and recovery date.

The daily control rule

Delivery progress and commercial progress are measured separately. A completed automation or post is a work output. A qualified inquiry requires expressed interest, need or timing from an ICP-matched practice. A booking requires a confirmed appointment in CQL.

No completion is prefilled.
All future actuals start blank.
CQL remains the sales record.

Exact calendar: 56 execution days, including 40 weekdays; 38 planned workdays after the proposed Nov 26-27 closure. Two review days follow. The inherited "60-day" label is retained as the program name.

Basis: DSI Reset v7, sections 5, 10, 14-17; Original proposal, pages 2-4. Intermediate pace and inquiry goal are planning additions.

Responsibility map: one accountable program owner

All eight internal lane owners report to Wyline. Two setters report to Nova. DSI owns approvals, closing and the trial experience.

CEO

Receives the Friday scoreboard. Decisions are routed through Wyline.

WYLINE / PROGRAM DIRECTOR

Daily targets, launch decisions, QA acceptance, blockers, recovery assignments and the client readout.

Nova

Conversion
Replies, call coverage, bookings, attendance.
20h/week + setters

Kenneth

Message
Voice, scripts, proof, copy and approved social.
12h/week

Emman

AI builds
Build, test, handoff, monitor and rollback.
20h/week

Alvin

CQL
Stages, calendars, reminders, referrals, social mirror.
10h/week

Joey

Data
Verified pool, suppression, real sender setup and QA.
15h/week

Dexter

LinkedIn
Replies, follow-ups, eligible requests and posting.
15h/week

Ludwig

Integrations
Webhooks, endpoints, retries and error recovery.
8h/week

Brian

Web
One-case page, forms, calendar embed and tracking.
10h build week; later by request

NIC / DSI OWNER

Approves the offer, sender identity, calendar, proof and spend. Holds booked conversations, closes the next step and calls the five Tier A accounts.

MASEEHA / DSI ACCOUNTS

Requests introductions and coordinates kits, case receipt, delivery, Day-30 reviews and approved referral credits. Updates the case handoff for Nova.


Internal output acceptance: Wyline.
Commercial/clinical decisions: Nic.
Trials and account logistics: Maseeha.

NOVA > SETTER 1 + SETTER 2 | Named roster required; cover 8:00 am-5:00 pm PT; reply <=15 min, positive inquiry call <=60 min.

Basis: supplied Responsibility Chart; Reset v7, sections 6 and 14. Backup routing is a proposed operating assignment.

Gantt: the full delivery window

A phase has a planned date and an acceptance gate. Passing time never marks a gate complete.

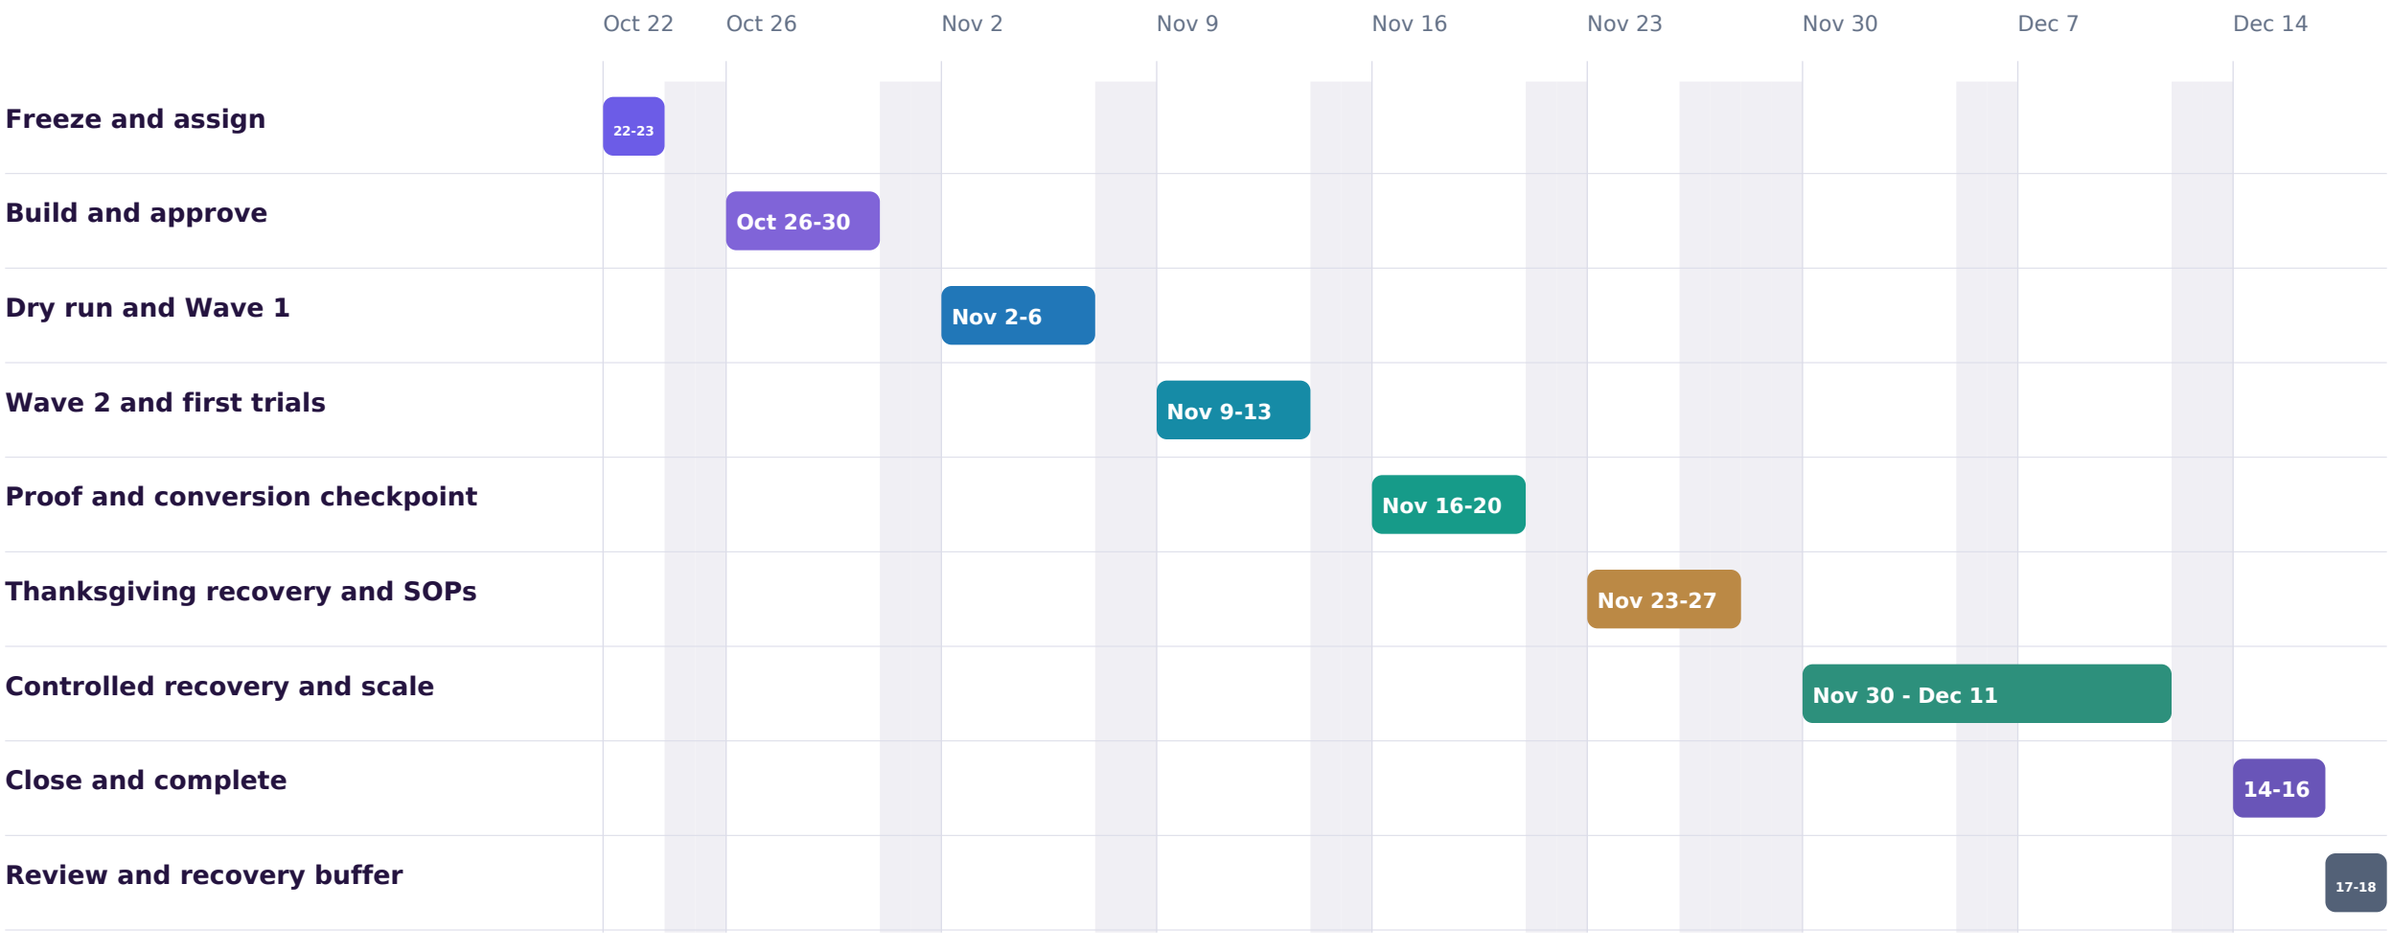

Oct 27
Nic decisions

Oct 30
Launch acceptance

Nov 2
Dry run

Nov 3
First sends

Nov 20
8 booked / 2 trials

Dec 16
Execution cutoff

Basis: Reset v7, sections 5 and 15; user cutoff Dec 16. Weekends and proposed holiday closure are shown as non-routine work.

Commercial flow: inquiry to received trial case

One practice, one CQL record, one next step. Referral and LinkedIn bookings are included inside the total.

750 verified

JOEY
NPI / site / zone / verified email / suppression / one true fact

40 inquiries

NOVA + SETTERS
ICP matched and expressed relevant interest, need or timing

20 bookings

NOVA > NIC
Qualified call or visit confirmed; unique opportunity counted once

15 held

NIC + NOVA
Meeting occurred and next step logged; future appointments excluded from due-held rate

6 trial cases

MASEEHA
Count only once the case is received by DSI. A kit request or promised case is not a trial start.

Day-30 review

NIC + MASEEHA
Schedule from the actual trial start. Late-November/December cohorts continue after this sprint.

Recurring account

NIC
Count the signed recurring plan with the source-defined review complete. Keep the 1-3 goal cohort-dependent.

First wins

By Nov 6: 4 qualified inquiries, 2 booked appointments and 1 held conversation. These are early working checkpoints; misses trigger same-day recovery.

Response and handoff standard

During staffed Pacific hours: human reply within 15 minutes; positive inquiry called within 60 minutes; same-day referral contact using the referrer's name. Every interested record has an owner, next step and due time.

Basis: Original proposal, pages 2-4; Reset v7, sections 7, 9-10 and 16-17. Overall inquiry goal/conversion assumption is proposed.

Daily control: close the work with proof

Wyline owns acceptance. Each lane owner supplies one output, one number and one help request.

Time	Owner	Required action
07:00 PT	Joey / Emman	Approved sending queue and LinkedIn list ready; planned new emails plus due follow-ups stay within mailbox caps.
08:00 PT	Nova / Setter 1 / Setter 2	Pacific business-hour coverage opens. Alert acknowledged within 5 min; human reply within 15 min; positive called within 60 min.
09:00 PT	All internal owners	15-minute standup: shipped output, one KPI, one blocker/help request. Wyline assigns rescue owner and recovery date.
13:00 PT	Nova / Wyline	SLA and blocked-task check; invoke backup before a missed commitment.
16:45 PT	All owners	Enter actual output, proof link, status, blocker and next step. No self-certified acceptance.
17:00 PT	Wyline	Accept evidence or return to owner; retain original due date, carry unfinished task forward visibly and assign recovery date.

Ready
Dependencies are cleared

→

In progress
Owner is executing

→

Review
Actual + evidence ready

→

Accepted
Reviewer accepts proof

Blocked or missed: record the reason, help needed, recovery owner and recovery date. Keep the original deadline. A deferred task remains unfinished; a new date never erases the miss.

Basis: Reset v7, sections 6, 9 and 14; recovery fields and acceptance workflow are planning additions.

Targets: a visible trajectory for the team

Cumulative goals, not forecasts. Weekly increments and the inquiry goal are proposed pacing; the reset endpoints come from the source plan.

By date	Verified pool	Qualified inquiries	Booked	Held	Trials received	Referral intros
Oct 30	250	0	0	0	0	0
Nov 6	500	4	2	1	0	3
Nov 13	500	10	5	3	1	5
Nov 20	500	16	8	6	2	8
Nov 25	500	16	8	6	2	8
Dec 4	650	28	14	10	4	12
Dec 11	750	40	20	15	6	15
Dec 16	750	40	20	15	6	15

Rate goals

100% response SLA | >=75% final held rate | >=3% human email reply rate | >=1.5% positive email reply rate. Keep the proposal's 2-5% positive-reply benchmark visible alongside the reset threshold.

Attribution rule

Referral-sourced bookings: 8. LinkedIn DM bookings: 8. Both sit inside the 20 total; assisted channels are tagged separately and never added again.

Basis: Reset v7, section 10; original proposal pages 3-4. Booked = all sources combined, with source subsets shown separately in the tracker.

Launch gate: deliver by Oct 30, rehearse Nov 2

First controlled sends: Nov 3. Hard commercial/data gates must pass; a tested manual process can replace delayed automation.

Owner	What must be ready	Acceptance evidence
Wyline / Nic	Written decisions	Sender authorization, offer and case limits, proof permissions, calendar slots, client capacity and spending decision.
Joey	250 verified contacts	NPI/site/zone/email checks; suppression; 50-row sample >=95% dental and >=95% in zone; zero twice-fatigued contacts.
Kenneth	Approved copy pack	Voice guide, 3 emails, LinkedIn sequence, phone script, 10 replies, 8 objections and one-case page copy.
Nova / setters	Staffed conversion lane	Two named setters; 8am-5pm coverage; three role plays each; reply <=15 min and positive call <=60 min.
Alvin / Nova	CQL end-to-end test	Booking, reminders, no-show recovery, trial stages and Day-30 task proved with a dummy lead.
Emman / Ludwig	Inbox or tested manual path	38-reply test set; >=90% classification; >=60% drafts acceptable; alert <60 sec; retry, monitoring and fallback.
Brian / DSI	Page + forms + tracking	Approved page live; form creates CQL record with source; calendar and confirmation tested; no unapproved proof.
Dexter / Alvin	LinkedIn + social queue	Eligible first 25; stage mapping; real-account authorization; approved exact posts; approved mirrors only.

Proof assets delayed? Hold affected proof claims and follow-ups. Site access delayed? Hold page links. Log the affected lane and approved workaround; do not mark the whole gate green without evidence.

Basis: Reset v7, section 15. Manual fallback may remove an automation delay; it does not waive sender authorization, approved claims or response coverage.

Oct 22 - Nov 6: build, approve, launch

Day map for the shared standup. Detailed per-person deliverables, acceptance criteria and dependencies are in the live tracker and workbook.

Date	Day type	Main delivery or decision	Cumulative goal
Oct 22 Thu	Execution	Freeze old activity and name ownership	0 inquiry / 0 booked / 0 trial
Oct 23 Fri	Execution	Coverage roster and build design	0 inquiry / 0 booked / 0 trial
Oct 24 - Oct 25	Weekend	No routine assignments. Existing warm-ups/approved automations only; any exception needs explicit coverage.	-
Oct 26 Mon	Execution	Build and approve	0 inquiry / 0 booked / 0 trial
Oct 27 Tue	Execution	DSI written approvals	0 inquiry / 0 booked / 0 trial
Oct 28 Wed	Execution	250-contact list QA	0 inquiry / 0 booked / 0 trial
Oct 29 Thu	Execution	Copy and operating pack approved	0 inquiry / 0 booked / 0 trial
Oct 30 Fri	Execution	Launch go/no-go	0 inquiry / 0 booked / 0 trial
Oct 31 - Nov 1	Weekend	No routine assignments. Existing warm-ups/approved automations only; any exception needs explicit coverage.	-
Nov 2 Mon	Execution	Timed full dry run	0 inquiry / 0 booked / 0 trial
Nov 3 Tue	Execution	Wave 1 live	1 inquiry / 0 booked / 0 trial
Nov 4 Wed	Execution	Dry run and Wave 1	2 inquiry / 1 booked / 0 trial
Nov 5 Thu	Execution	Dry run and Wave 1	3 inquiry / 1 booked / 0 trial
Nov 6 Fri	Execution	500 verified and assists accepted	4 inquiry / 2 booked / 0 trial

Basis: Reset v7, sections 5 and 15; daily allocations after Nov 6 are proposed. Dates shown in the 2026 Pacific calendar.

Nov 7 - Nov 20: conversations and trials

Day map for the shared standup. Detailed per-person deliverables, acceptance criteria and dependencies are in the live tracker and workbook.

Date	Day type	Main delivery or decision	Cumulative goal
Nov 7 - Nov 8	Weekend	No routine assignments. Existing warm-ups/approved automations only; any exception needs explicit coverage.	-
Nov 9 Mon	Execution	Wave 2 and first trials	5 inquiry / 2 booked / 0 trial
Nov 10 Tue	Execution	Wave 2 and first trials	6 inquiry / 3 booked / 0 trial
Nov 11 Wed	Execution	Wave 2 and first trials	7 inquiry / 3 booked / 0 trial
Nov 12 Thu	Execution	Scoreboard automation accepted	8 inquiry / 4 booked / 0 trial
Nov 13 Fri	Execution	A/B referral asks complete	10 inquiry / 5 booked / 1 trial
Nov 14 - Nov 15	Weekend	No routine assignments. Existing warm-ups/approved automations only; any exception needs explicit coverage.	-
Nov 16 Mon	Execution	Proof and conversion checkpoint	11 inquiry / 5 booked / 1 trial
Nov 17 Tue	Execution	Proof and conversion checkpoint	12 inquiry / 6 booked / 1 trial
Nov 18 Wed	Execution	Proof and conversion checkpoint	13 inquiry / 6 booked / 1 trial
Nov 19 Thu	Execution	Client Reporter accepted	14 inquiry / 7 booked / 1 trial
Nov 20 Fri	Execution	Midpoint funnel decision	16 inquiry / 8 booked / 2 trial

Basis: Reset v7, sections 5 and 15; daily allocations after Nov 6 are proposed. Dates shown in the 2026 Pacific calendar.

Nov 21 - Dec 4: callbacks and controlled recovery

Day map for the shared standup. Detailed per-person deliverables, acceptance criteria and dependencies are in the live tracker and workbook.

Date	Day type	Main delivery or decision	Cumulative goal
Nov 21 - Nov 22	Weekend	No routine assignments. Existing warm-ups/approved automations only; any exception needs explicit coverage.	-
Nov 23 Mon	Reduced activity	Thanksgiving recovery and SOPs	16 inquiry / 8 booked / 2 trial
Nov 24 Tue	Reduced activity	Thanksgiving recovery and SOPs	16 inquiry / 8 booked / 2 trial
Nov 25 Wed	Reduced activity	All 41 existing-account asks complete	16 inquiry / 8 booked / 2 trial
Nov 26 - Nov 27	Holiday	No routine assignments. Existing warm-ups/approved automations only; any exception needs explicit coverage.	-
Nov 28 - Nov 29	Weekend	No routine assignments. Existing warm-ups/approved automations only; any exception needs explicit coverage.	-
Nov 30 Mon	Execution	Controlled recovery and scale	18 inquiry / 9 booked / 2 trial
Dec 1 Tue	Execution	Controlled recovery and scale	20 inquiry / 10 booked / 2 trial
Dec 2 Wed	Execution	Controlled recovery and scale	23 inquiry / 11 booked / 3 trial
Dec 3 Thu	Execution	Controlled recovery and scale	25 inquiry / 12 booked / 3 trial
Dec 4 Fri	Execution	December recovery checkpoint	28 inquiry / 14 booked / 4 trial

Basis: Reset v7, sections 5 and 15; daily allocations after Nov 6 are proposed. Dates shown in the 2026 Pacific calendar.

Dec 5 - Dec 18: complete the work and close

Day map for the shared standup. Detailed per-person deliverables, acceptance criteria and dependencies are in the live tracker and workbook.

Date	Day type	Main delivery or decision	Cumulative goal
Dec 5 - Dec 6	Weekend	No routine assignments. Existing warm-ups/approved automations only; any exception needs explicit coverage.	-
Dec 7 Mon	Execution	Controlled recovery and scale	30 inquiry / 15 booked / 4 trial
Dec 8 Tue	Execution	Controlled recovery and scale	32 inquiry / 16 booked / 4 trial
Dec 9 Wed	Execution	Controlled recovery and scale	35 inquiry / 17 booked / 5 trial
Dec 10 Thu	Execution	Controlled recovery and scale	37 inquiry / 18 booked / 5 trial
Dec 11 Fri	Execution	Full target checkpoint	40 inquiry / 20 booked / 6 trial
Dec 12 - Dec 13	Weekend	No routine assignments. Existing warm-ups/approved automations only; any exception needs explicit coverage.	-
Dec 14 Mon	Execution	Close and complete	40 inquiry / 20 booked / 6 trial
Dec 15 Tue	Execution	Close and complete	40 inquiry / 20 booked / 6 trial
Dec 16 Wed	Execution	Final execution deadline	40 inquiry / 20 booked / 6 trial
Dec 17 Thu	Review buffer	Review and recovery buffer	40 inquiry / 20 booked / 6 trial
Dec 18 Fri	Review buffer	Review and recovery closeout	40 inquiry / 20 booked / 6 trial

Basis: Reset v7, sections 5 and 15; daily allocations after Nov 6 are proposed. Dates shown in the 2026 Pacific calendar.

Responsibility and handoff matrix

A = accountable decision owner. R = person responsible for execution. S = support. Every handoff ends with a CQL link or deliverable evidence.

Workstream	A	R	S	Handoff / proof
Daily program / final acceptance	Wyline	Wyline	All lane owners	CEO receives weekly report
Verified pool / safe send queue	Wyline	Joey	Kenneth / Ludwig	Nova + Dexter receive approved records
Copy / proof / social drafts	Wyline	Kenneth	Nic / Maseeha	Dexter + Alvin publish exact approved versions
Human reply / phone / bookings	Wyline	Nova + setters	Kenneth / Emman	Nic gets qualified booking + prep brief
CQL / reminder / referral workflow	Wyline	Alvin	Nova / Ludwig	Every record has next step + due time
AI / integration reliability	Wyline	Emman + Ludwig	Lane owner / Alvin	Operator accepts test + SOP + rollback
Page / form / tracking	Wyline	Brian	Kenneth / Alvin	Nova receives test lead
LinkedIn actions	Wyline	Dexter	Joey / Kenneth	Interested replies to Nova immediately
Sales meeting / commercial close	Nic	Nic	Nova / Maseeha	Trial decision and conditions logged
Referral asks / trial logistics	Nic	Maseeha	Nova / Alvin	Case receipt, delivery and review dates
Paid media / spend approval	Nic	Wyline	Kenneth / Brian / Alvin	Written cap + tested tracking before spend

Basis: supplied responsibility chart and Reset v7, sections 6, 14 and 16-17. Proposed recovery routing is included in the tracker.

Automation supports the lane; acceptance proves it

Eight named support tools. Humans approve messages, make calls and execute LinkedIn actions.

Tool	Operating owner	Due	Acceptance test
Scout	Joey	Oct 30	50 random rows: >=95% confirmed dental, >=95% in zone, zero twice-touched contacts; include NPI, site and email evidence.
Writer	Kenneth	Oct 29	20 sample contacts; >=80% first lines approved unedited; zero invented claims.
Inbox	Nova	Oct 30	8 real +30 synthetic replies; >=90% classifications correct; >=60% drafts acceptable unedited; alert <60 sec; human send always.
Follow-up	Nova	Oct 30	Dummy lead receives approved booking/reminder flow in order; 24 h/2 h reminders; no-show rebook <=10 min; kit and Day-30 tasks; honor consent/suppression.
Phone Assist	Nova	Nov 6	Brief > human call > log > follow-up cycle under 6 minutes admin; CQL next step present.
LinkedIn Assist	Dexter	Nov 6	Daily verified eligible list by 07:00 PT; Kenneth-approved drafts; zero automated LinkedIn actions.
Scoreboard	Wyline	Nov 12	Three consecutive days exactly reconcile to Wyline manual source counts; no zero substitution for missing actuals.
Client Reporter	Wyline	Nov 19	Wyline edit <10 minutes; valid dates; reconciled counts; zero placeholders/unsupported claims.

If automation misses its accepted handoff, use the tested manual SOP and log the repair. The conversion queue keeps a named human owner.

Basis: Reset v7, section 7. Weekend dates moved to the preceding workday in the source runbook.

Proposal alignment: the recovery actions behind the promise

The original proposal supplies the commercial objective. The reset supplies the immediate execution sequence.

Original commitment	Proposal basis	Reset execution	Owner
Qualified dental pipeline	100+ interested ICP leads over 6 months	750 verified records + proposed 40 qualified inquiries in this reset	Joey / Nova
Email + real-person LinkedIn	One coordinated contact and handoff system	Real senders; one approved offer; suppression; CQL record across channels	Joey / Dexter / Nova
Appointments and trials	52-84 booked; 18-30 trials over 6 months	Recover toward 20 booked, 15 held and 6 received trials by cutoff	Nova / Nic / Maseeha
Controlled trial and retention	Defined 30-day trial; review; recurring plan	Nic approves revised First Case Guarantee; preserve qualification and Day-30 follow-through	Nic / Maseeha
Scripts, lead handoff and reports	Sales scripts, checklist, monthly KPI view	Daily evidence, weekly decisions, response SLA, call coaching and source reconciliation	Kenneth / Nova / Wyline
Referral process	Approved benefit and qualified introduction	41 account asks; 15 introductions; 8 referral bookings inside the total20	Maseeha / Nic
Commercial scope	40 outreach hours/month in recommended proposal; excluded items require approval	Reset hours are internal planning capacity; record any separate cost decision; ads start at $0	Wyline / Nic

Basis: DSI 6-Month Client Acquisition & Retention Proposal v2, pages 1-7; DSI Reset v7. Operating ranges are targets, not recorded achievements.

How Wyline runs this tomorrow morning

One live operating record. The workbook is a portable planning copy; it does not automatically synchronize with the site.

Step	Action	What it means
1	Select the date and owner	Read the exact deliverable, target mode, gate and evidence needed. Use the recovery queue before starting new low-priority work.
2	Record the result	Enter actual output and link proof. Use a CQL record or approved artifact; keep patient data out of the task note.
3	Move to Review	The operator submits the task. Wyline or her recorded delegate accepts or returns it. A capacity ceiling is not a forced sending quota.
4	Rescue unfinished work	Write the blockage, help needed, recovery owner and next deadline. Preserve the original date; report the miss honestly.
5	Read the outcome board	Compare deduplicated inquiries, booked, due/held meetings and received cases with pace. Investigate the failing conversion step.
6	End the day	Confirm tomorrow coverage and appointments, reconcile the scoreboard with CQL and make the next-day work visible.

REPLY LANE

SLA slips

Nova takes the queue; activate named backup; throttle new intake.

NO APPOINTMENTS

Qualified inquiries fail to book

Review call recordings, calendar availability and one script variable.

BUILD DELAY

Tool is not ready

Use the tested manual process; Emman owns the repair and new date.

Friday review: 45 minutes, decisions only. Report results, misses and recovery ownership to the CEO and DSI after Wyline checks the exact figures. Routine weekends are off; holiday coverage is confirmed with the client.

Basis: source role cards and stop rules; workflow, risk routing and file-use rules are proposed execution controls.
